BRHAT BANGALORE MAHANAGARA PALIKE

INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Providing Electrical Poles and Street lights in Ward No-11 Kuvempunagara Vidyaranyapura Sub Division	
2	Estimate Cost	15.00 Lakhs	
3	Administrative Approved No and Date	BBMP/CE/YZ/AS/97A/15-16, Date. 01.01.2016.	
4	Technical sanction No. and Date	BBMP/EE/ELE/YZ/TS/04/15-16, Date.01.01.2016.	
5	Job Code No. and P Code No.	011-16-000017	
6	Tender Direct Entrested to KRIDL	Not Applicable	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	EE/BTP/BBMP/E-PMT/03/2015-16, Dated:22.01.2016 (Revised)	
8	Tender Approved Details	CE Approval Dated:17.07.2016.	
9	Work Order No and Date	EE/BTP/BBMP/E-PMT/258/2015-16, Dated:26.09.2016. EE/ELE/YZ/RWO/19/2016-17, Dt:16.07.2016.	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	16.07.2016	
12	Actiual Date of Completion	15.10.2016	
13	Delay if any	Nil	
14	Reson for Delay	Nil	

Executive Engineer
Electrical Division
Yelahanka Zone BBMP

15	**Payment made till date.**	Nil	
16	**Status of Work**	Completed	
17	**Photograph verfied**	Enclosed	
18	**Date of Inspection**	17.12-16 ~~20-09-2016~~	
19	**MB No. and Page No.**	MB No. ~~3102~~ 3107 Page No. ~~310187 to 310190~~ 310672-684	
20	**BR No. and Date**	113/16-17 Dated:16/09/2016	
21	**Section officer**	Sri Babu Reddy.K.N J.E	
22	**Sub Division Officer**	Sri K.Nagesh AEE	
23	**Observation**		
a	**Work Quality**	Satisfactory	
b	**Comments**	Work completed as per MB	

Y.C.KALEGOWDA.
Rtd Executive Engineer
3rd Party Inspection (Works)
BBMP Yelahanka Zone

Executive Engineer
Electrical Division
Yelahanka Zone BBMP
Byatarayanapura, Bangalore-92

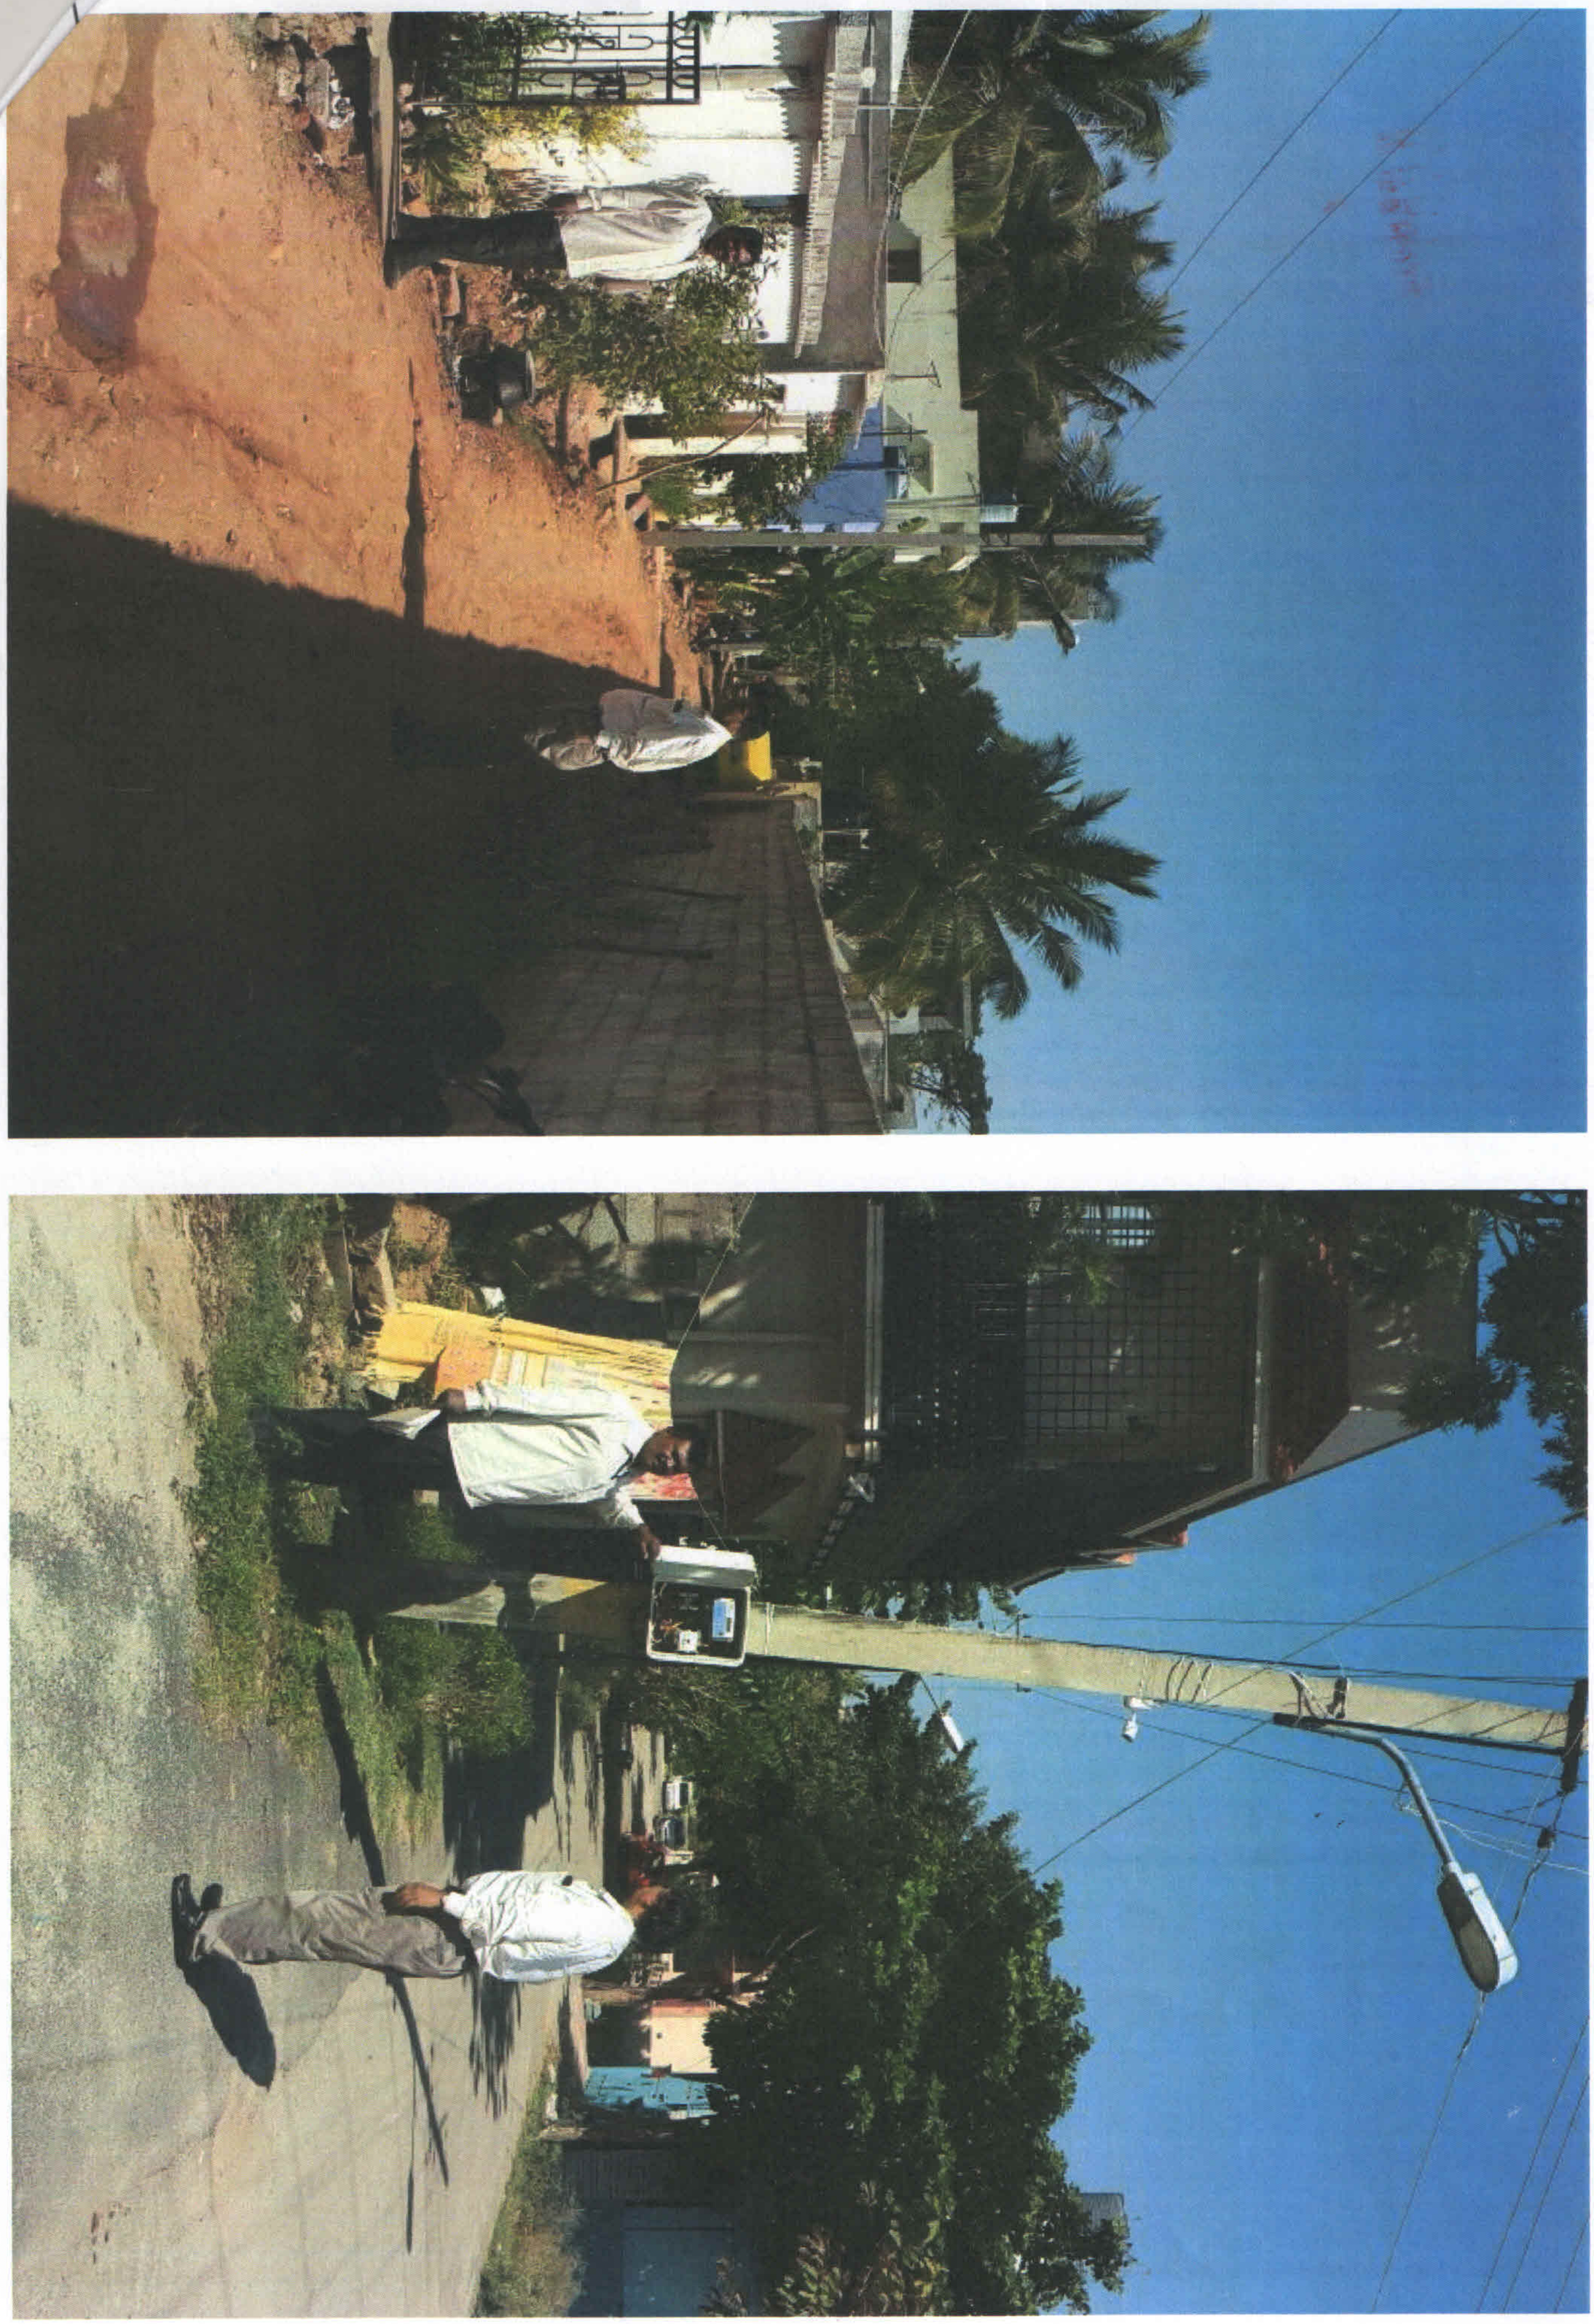

Y.C.KALEGOWDA.
Rtd Executive Engineer

Executive Engineer
Electrical Division
